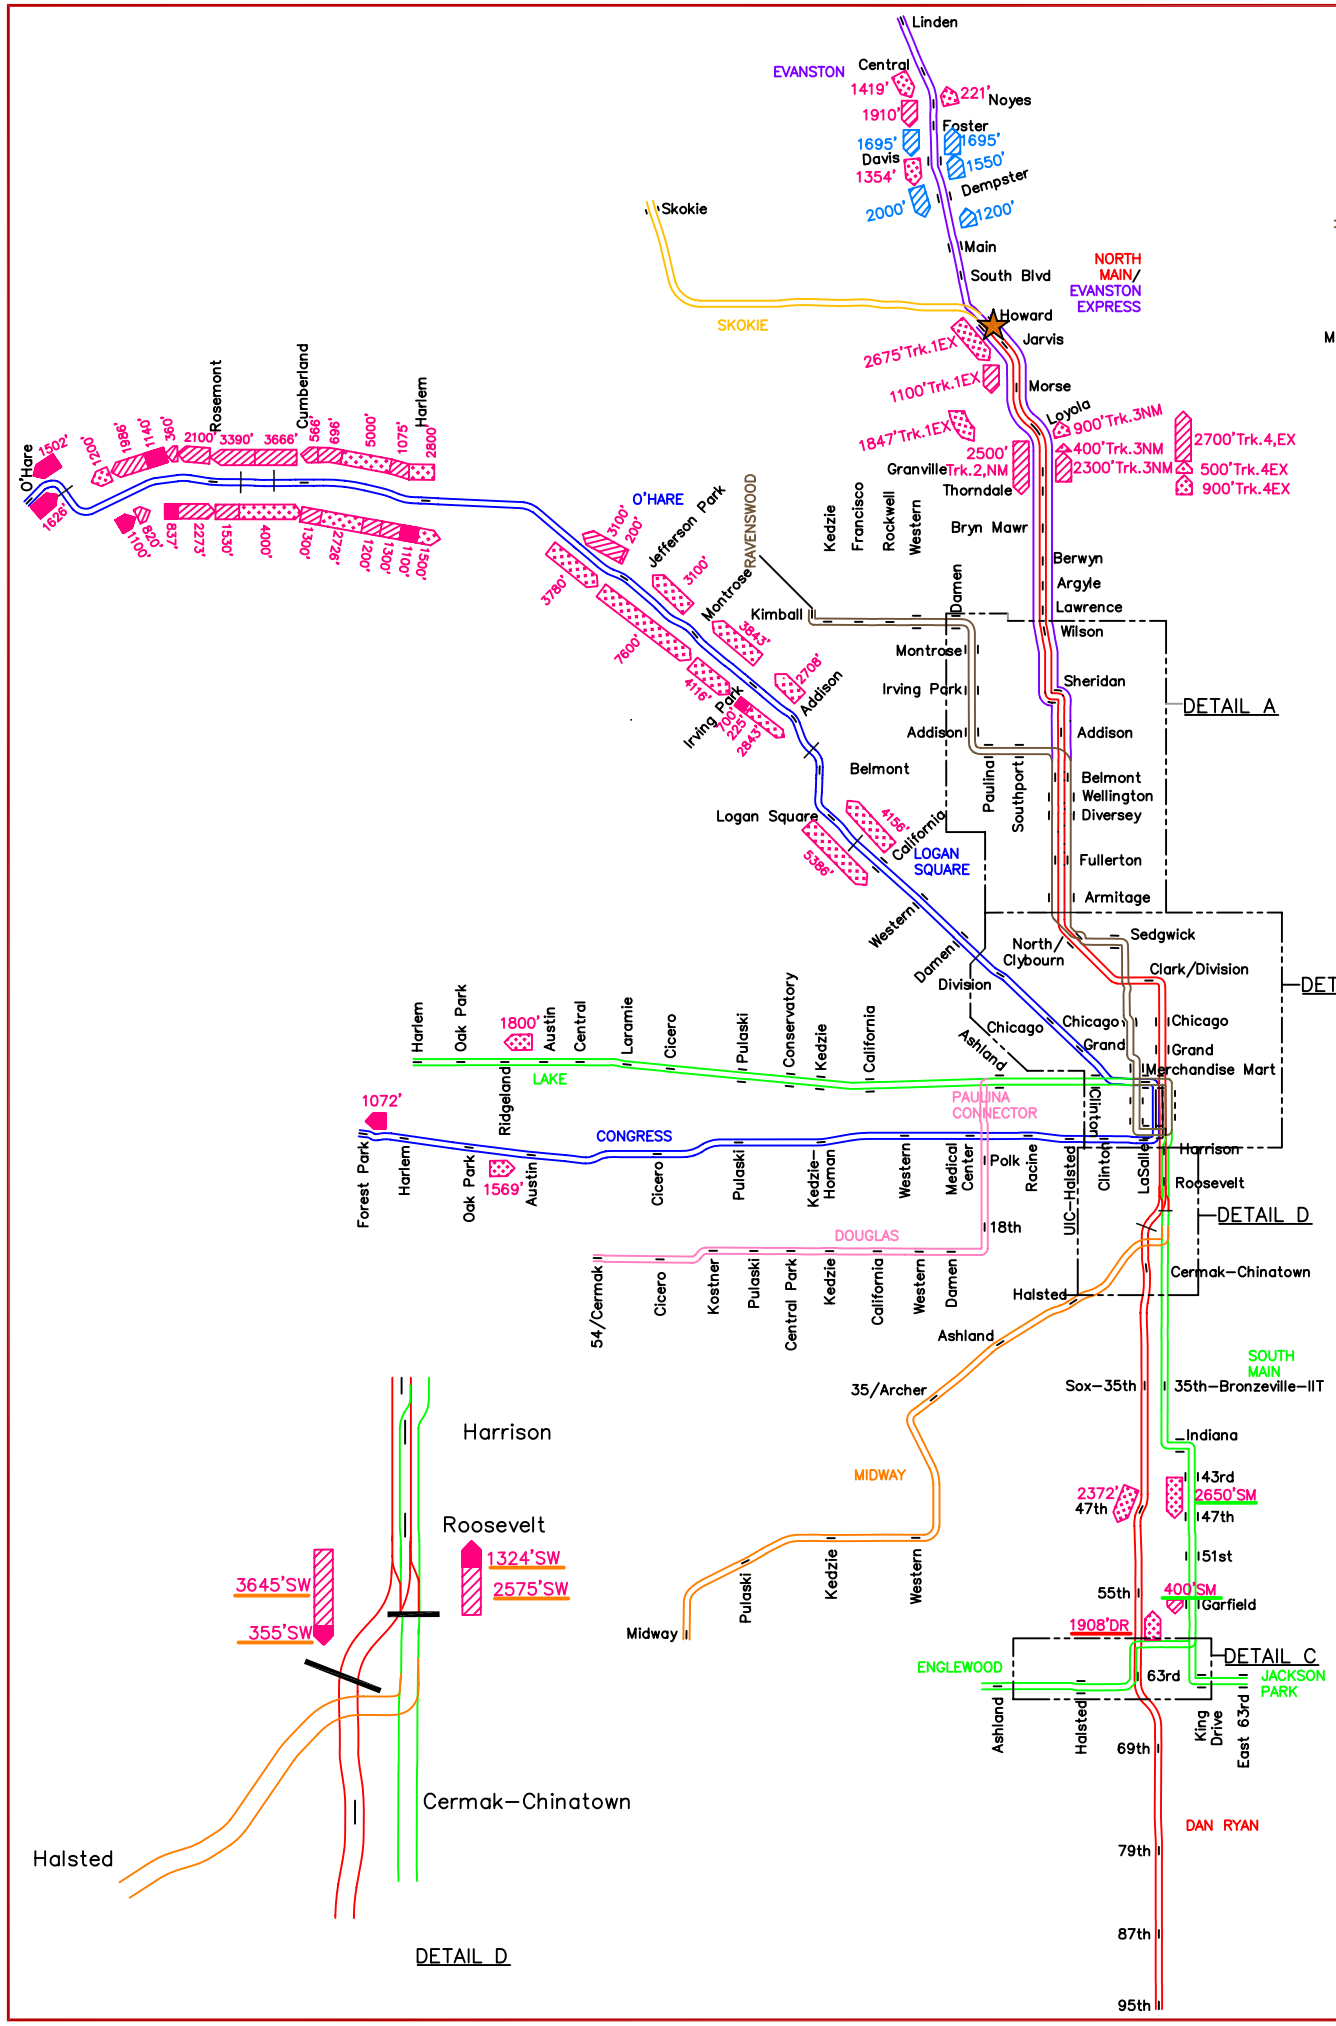

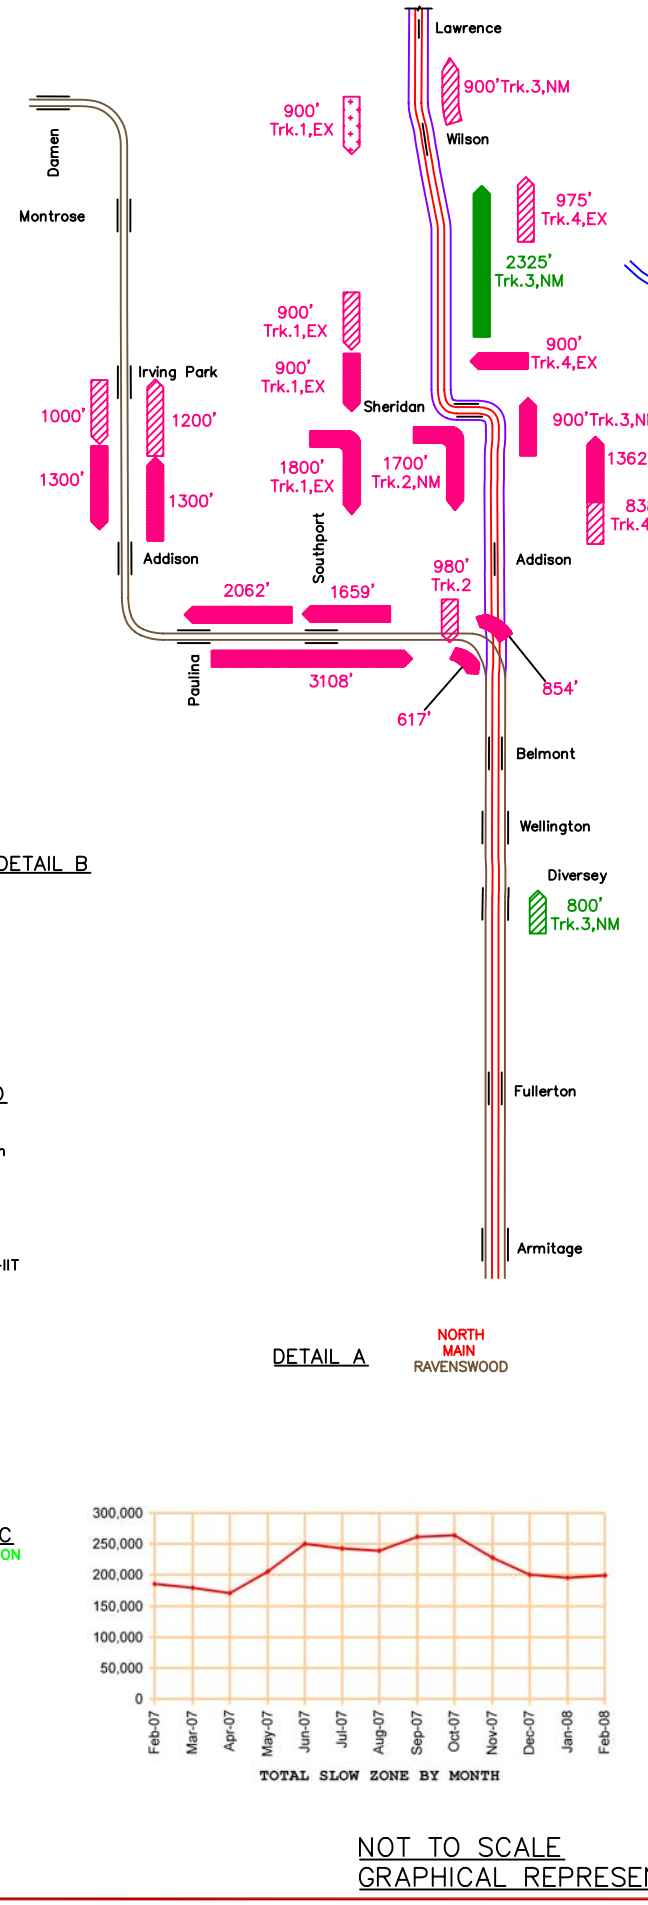

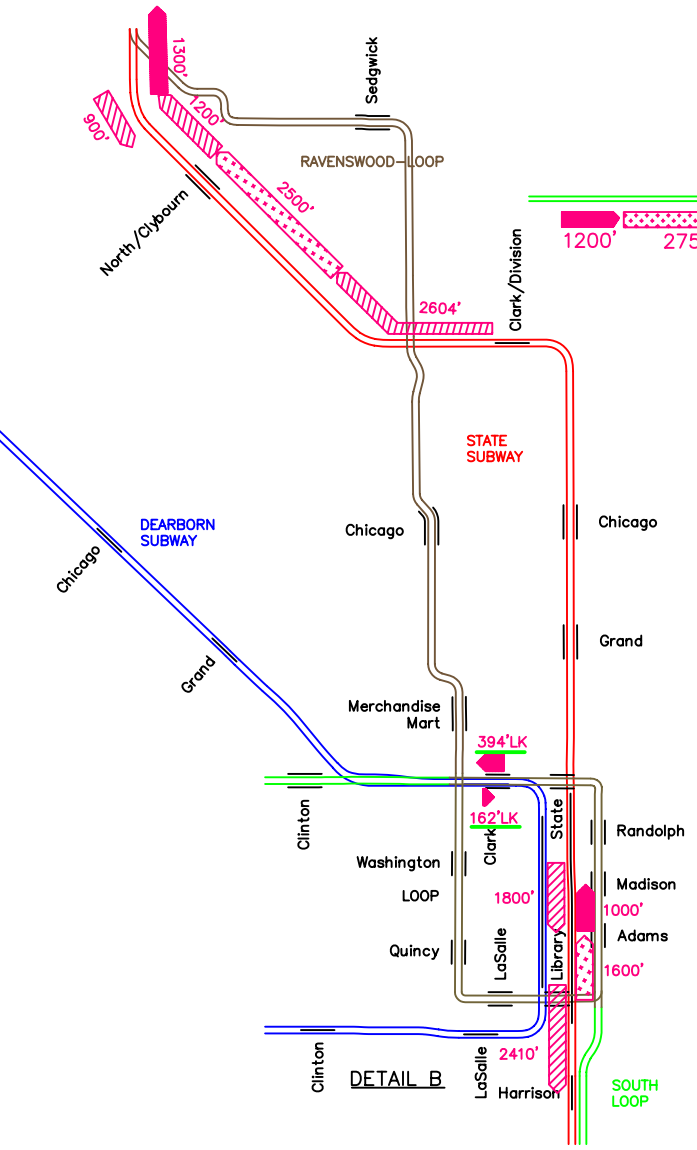

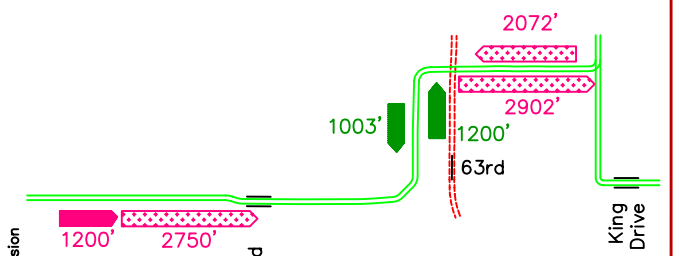

SLOW ZONE BY AREA				
Track (CTA)	15 mph	36,218	182,802	
	25 mph	55,265		
	35 mph	91,319		
Structure (CTA)	15 mph	0	8,140	
	25 mph	8,140		
	35 mph	0		
Signal (CTA)	15 mph	0	0	
	25 mph	0		
	35 mph	0		
Power (CTA)	15 mph	0	0	
	25 mph	0		
	35 mph	0		
Construction (CTA/Contractor)	15 mph	4,528	5,875	
	25 mph	1,347		
	35 mph	0		

★ NOTE: SIGNAL ISSUE RESULTING IN MULTIPLE 10 MIN. PLUS DELAYS DURING PREVIOUS MONTH

TOTAL SLOW ZONE TRACK

Rail Line	15 mph	25 mph	35 mph	Total Slow Zone	Linear Trk.-Ft.	% Slow	Movement Removed	Movement Added	Total SZ	% Slow
Congress	1,072	0	1,569	2,641	94,010	2.8	0	1,569	94,432	32.3
O'Hare/Logan Square	10,648	23,329	57,814	91,791	152,956	60.0	0	2,177		
Dearborn Subway	0	0	0	0	45,818	0	0	0		
North Main Line	4,925	8,927	900	14,752	78,966	18.7	0	0	34,442	14.9
State Subway	1,000	9,241	4,700	14,914	51,328	29.1	1,927	0		
Dan Ryan	0	0	4,776	4,776	101,332	4.7	1,844	0		
Skokie	0	0	0	0	52,146	0	0	0	0	0
Evanston	0	10,050	2,994	13,044	40,714	32.0	0	0	30,411	29.9
Evanston Express	4,962	6,013	6,392	17,367	60,970	28.5	0	0		
Loop	556	0	0	556	21,470	2.6	0	0	556	2.6
Ravenswood/Ravenswood-Loop	10,900	2,200	0	13,100	98,364	13.3	0	0	13,100	13.3
Midway/Grand Junction	3,280	4,619	0	7,899	99,224	8.0	0	0	7,899	8.0
Lake	0	0	1,800	1,800	93,114	1.9	0	1,800	15,977	7.8
South Loop/South Main Line	0	400	2,650	3,050	68,906	4.4	0	0		
Englewood	3,403	0	7,724	11,127	31,916	34.9	2,750	2,750		
Jackson Park	0	0	0	0	12,162	0	0	0		
Douglas/Paulina Connector	0	0	0	0	77,710	0	0	0	0	0.0
TOTALS	40,746	64,752	91,319	196,817	1,181,106	16.7	6,467	8,296		

NOT TO SCALE
GRAPHICAL REPRESENTATION

DATE	DESCRIPTION	
		IN CHARGE C.B.
		APPROVED BY B.M.jr
		CHECKED BY B.M.jr
		UPDATED BY S.M.
16 MAY 06	ORIGINAL	ORIGINATED BY J.J.H.
		Prepared by: Track Maintenance

CTA RAIL CUSTOMER IMPACT MAP

February 06, 2008
